31 January 2023

MEMORANDUM

From: Director, Facilities & Environmental

Subj: CNIC N4 PROJECT DEVELOPMENT AND ASSESSMENT GUIDE FOR SHORE PROGRAM OBJECTIVE MEMORANDUM, FISCAL YEARS 2026-2030 (POM-26)

Ref: (a) OPNAVINST 11010.20J, Navy Facilities Projects Instruction, 27 December 2022
(b) Shore Mission Integration Group Charter, 05 May, 2021
(c) Electronic Project Generator (EPG)/Integrated Priority List (IPL) MILCON Users Guide, January 2023
(d) Electronic Project Generator (EPG)/Integrated Priority List (IPL) Special Projects Users Guide, January 2023

Encl: (1) Shore Mission Integration Group (SMIG) Evaluation and Prioritization Process
(2) List of POM-26 Addendums

1. Purpose. This guide provides POM-26 project submission and prioritization information in accordance with references (a) and (b) and enclosure (1). Included are:
- Submission and assessment timeline
- Strategic Alignment and Guiding Principles (SA/GP) and Risk Assessment criteria
- Project submission guidelines
- EPG/IPL support documentation per references (c) and (d)
- Shore Mission Integration Group (SMIG) and SMIG Working Group (WG) assessment guidance provided in Addendums (1-8)

Please see enclosure (2) for a full list of addendums. For the purposes of this Guide, Budget Year (BY) refers to FY26, BY+1 refers to FY27, BY+2 refers to FY28, BY+3 refers to FY29 and BY+4 refers to FY30.

2. Applicability. This guide applies to all CNIC Installation and Region facility project proposals submitted for POM-26 consideration in accordance with the timeline outlined in Table 1 below and in the subsequent addendums. Region Commanders will lead a collaborative effort with Combatant Commanders (CCDRs), Navy Components (NCCs) and Lead Proponents/Warfare Enterprises/Providers (WE/P) to integrate all requirements within their Area of Responsibility (AOR). Facility projects, at Enduring or Contingency locations, include active and reserve Military Construction (MILCON), Unspecified Minor Construction (UMC), Laboratory Revitalization Program (LRP), Special Projects

(Sustainment, Restoration, and Modernization) and Energy. In addition, a Naval Construction Force (NCF) requirements data call is detailed in Addendum 7.

Activity	POM26
CNIC distribute DRAFT POM26 Project Development and Assessment Warning Order/Guide	**31-Jan-23**
2022 CNIC N4 Facilities Stakeholders Meeting	**7-9 Feb 2023**
CNIC distribute FINAL POM26 Project Development and Assessment Warning Order/Guide	**9-Mar-23**
Activity	**Dates**
Installations complete project assessment/enter installation investment prioritization in the IPL	31-Mar-23
Lead Proponent/COCOM/NCC and Region coordination	31 Mar - 28 Apr 23
Lead Proponents and stakeholders complete project assessment/enter investment prioritization in the IPL	28-Apr-23
Region (RMIG) complete project assessment in the IPL /Complete project rankings; CNIC initial review of Region investment priorities	23-May-22
Region submits POM26 project briefing documents and supporting documentation to CNIC	26-May-23
SMIG WG initial assessment: Region briefs / Score / Adjudicate SMIG WG initial assessment: Region briefs / Score / Adjudicate	5-9 June 2023/ 12-16 June 2023
SMIG WG Follow-on review and adjudication	Jul-23
CNIC N46 and NAVFAC CI begin coordination with OPNAV Resource Sponsors in anticipation of POM26 Sponsor Program Proposal (SPP) (MILCON only)	Jul-23
CNIC provides initial assessment results to Regional Commanders/SYSCOMs; Fleets provide to TYCOMs	Aug-23
Final SMIG assessment review/debrief	Oct-23
Final SMIG-approved IPL to stakeholders	Nov-23

Table 1

3. Roles and Responsibilities

a. Installation Commanding Officers. In accordance with Table 1, installations shall complete the actions in the subparagraphs below for POM-26 MILCON and Special Projects. UMC and NCF timelines are included in Addendums 4 and 7 respectively. Installations cannot make changes in the IPL once the installation submission is complete.

(1) Combatant Commanders (CCDRs)/Navy Components (NCCs) and Lead Proponent/Warfare Enterprise and Provider (WE/P) Coordination. Installations shall coordinate development of each project with supported Commands and tenants whose mission is supported by the project. Installations shall develop infrastructure solutions to mitigate vulnerabilities for any critical asset. After coordination, installations will identify the Lead Proponent/WE/P in EPG. In addition, once the project is linked to the IPL module, the Regions will have an opportunity to further clarify and assign Lead Proponents (i.e. WE/Ps) from a more comprehensive drop-down list in the IPL module not otherwise available in EPG (e.g. SSP). Lead Proponents/WE/P are unable to assess their projects in the IPL module until the project is linked to the appropriate Lead Proponent/WE/P. Where warranted, Secondary and Tertiary Lead Proponents/WE/P shall be indicated in the Facility Investment (MILCON/FSRM) Integrated Investment Plan and briefing documents as appropriate. Although CCDRs/NCCs cannot be mapped to a project within EPG or IPL, installations shall identify supported CCDR/NCC on the Project Data Sheet where appropriate. A list of CCDRs, Lead Proponents/WE/P is included in Tables 2 and 3 below.

Lead Proponents/Warfare Enterprises/Providers
Information Warfare Enterprise (IWE)
Naval Aviation Enterprise (NAE)
Navy Expeditionary Combat Enterprise (NECE)
Strategic Systems Programs(SSP)
Surface Warfare Enterprise (SWE)
Undersea Warfare Enterprise (USE)
Bureau of Medicine and Surgery (BUMED)
Commander Navy Installations Command (CNIC)
CNIC – N3 Operations
CNIC – N9 Fleet & Family Readiness
Manpower, Personnel, Training and Education (MPT&E)
Naval Air Systems Command (NAVAIR)
Naval Facilities Engineering Systems Command (NAVFAC)
Naval Sea Systems Command (NAVSEA)
Naval Supply Systems Command (NAVSUP)
Naval Information Warfare Systems Command (NAVWAR)
Special Warfare Command (SPECWAR)
Office of Naval Research (ONR)
Reserve Force (RESFOR)
Military Sealift Command (MSC)
Naval History and Heritage Command (NHHC)
Navy Munitions Command (NMC)
Naval Education Enterprise (NEE)

Table 2

Combatant Commands
United States Indo-Pacific Command (USINDOPACOM)
United States Special Operations Command (SOCOM)
United States European Command (EUCOM)
United States Central Command (CENTCOM)
United States Africa Command (AFRICOM)
United States Strategic Command (STRATCOM)
United States Transportation Command (TRANSCOM)
United States Southern Command (SOUTHCOM)
United States Northern Command (NORTHCOM)
United States United States Cyber Command (CYBERCOM)
United States Space Command (SPACECOM)

Table 3

(2) Updating Existing Projects. If a Region determines a project linked during POM-25 requires updating for POM-26, installations should **not** unlink the project, which will delete the project from the IPL. The installation shall instead update the IPL-linked version or another version of the project in EPG as described in reference (c) and (d).

(3) New Project Submission. All new projects shall have a DD-1391 completed in EPG and linked to IPL. This DD-1391 will contain a draft description "Installation/PWD DD-1391 with cycle "POM-26" or "SMIG PRI DD-1391" (MILCON only) with cycle POM-26 (for FY26/FY27 exception projects being considered for Budget PRI funding).

(4) NAVFAC MTP3 Process Requirements. Installations are required to complete the applicable Facility Planning Document (FPD) and Basic Facility Requirement (BFR) for the project category code and Unit Identification Code (UIC). The FPD and BFR data must be complete at the installation/SMIG PRI (MILCON only) DD-1391 status level. For all MILCON and Special Projects, installations will ensure the applicable FPD and BFR are attached in EPG (using the Electronic Document Management System), which justifies the necessary construction, demolition, or repair of a facility. MILCON projects require the BFR and FPD to be up-to-date and accurate for NAVFAC HQ/Echelon III review.

b. Commander, Navy Installations Command (CNIC). CNIC shall review and assess project submissions for MILCON, Special Projects, and UMC. As the shore integrator, CNIC is required to provide a consistent, systematic, and deliberate approach to identify investment requirements that close capability gaps and maximize fleet readiness. CNIC project reviews shall include

coordination with the Lead Proponents/WE/P to verify the validity of requirements, arbitrate differences and ensure project data sheets provide the detailed information required to allow projects to be rated, assessed and prioritized consistent with CNO Guidance and Risk Assessment-Severity criteria.

c. CCDRs/NCCs, Lead Proponents/Warfare Enterprises, Providers (WE/P) and Reserve Force (RESFOR). The Lead Proponent/WE/P or RESFOR shall review, validate, and prioritize projects for which they are the lead in accordance with the dates outlined in Table 1. In addition, if a Lead Proponent/WE/P has equity in a capital improvement project for which they are not the lead project proponent, but a stakeholder, there is a text block in the supplemental tab of the IPL module to capture other stakeholder endorsements (e.g. Surface Warfare Enterprise may endorse a Naval Sea Systems Command project). Where warranted, Secondary and Tertiary Lead Proponents/WE/Ps shall also be indicated in the Integrated Investment Plan and project data sheet.

(1) SMIG WG Briefs. CCDRs/NCCS/Lead Proponents/WE/P and RESFOR will be provided the opportunity to brief the SMIG WG on their enterprise capital improvement priorities prior to the SMIG WG assessment offsite meeting. CCDRs/NCCs/Lead Proponent/WE/P briefs should focus on capability gaps, mission impacts, and the requirements and capabilities the warfighter will gain by the proposed projects. Project briefs should not focus on project details such as scope and design features and should have minimal overlap with the Region briefs. CNIC will provide a classified setting to conduct these briefs if needed. Stakeholders shall provide a single prioritized Integrated Investment Plan for their requirements regardless of resource sponsor. In addition, all stakeholders will be invited to attend the SMIG WG assessment offsite virtually.

(2) Reviewing Project Submissions. Lead Proponent/WE/P and RESFOR will have view rights to all projects in order to identify any missing requirements and correct projects which have the incorrect Lead Proponent/WE/P identified. If it is determined a project is missing or an incorrect Lead Proponent/WE/P is listed, the Lead Proponent/WE/P/RESFOR shall coordinate with the applicable Region to correct. Lead Proponent/WE/P/RESFOR shall check the "Enterprise Status" block in IPL when they have completed their project assessment. If the Lead Proponent/WE/P/RESFOR is incorrect and cannot be resolved at the Region level, discrepancies shall be brought to CNIC N4 to resolve.

(3) Requirements Prioritization. While briefs with a priority list (and signed letters) are welcomed, the primary Lead Proponent/WE/P must mirror the prioritization they enter in the IPL

module as it will serve as the authoritative input to CNIC and its Regions. Any submission for consideration during POM-26 shall be submitted to CNIC, its affected Region and uploaded in iNFADS in accordance with the POM-26 timeline (Table 1) to give ample time for Regions to review during their RMIGs.

d. Region Commanders. Regions shall use a formally established Region Mission Integration Group (RMIG) to develop Integrated Investment Plan recommendations based on CNO Strategic Guidance and Risk Assessment criteria in alignment with Addendum 5 and in coordination with supported Lead Proponents/WE/Ps. To the greatest extent possible, Regions shall coordinate and schedule RMIGs with the intention of enabling maximum Lead Proponents/WE/P participation. An RMIG calendar including dates and times of RMIG and RMIG Working Group meetings across the Enterprise will be sent SEPCOR to help mitigate schedule conflicts.

(1) Assessing. As directed by Region Commanders, RMIGs shall use criteria and approved weightings in Addendum 1 to assess and prioritize MILCON, Special Projects and UMC requirements. Regions, supported by the RMIG, shall be expected to use the web-based version of Decision Lens to assess their MILCON, Special projects and UMC requirements.

(2) SMIG WG Briefs. Regions will brief the SMIG WG in accordance with the guidance delineated in Addendums 1-4. Regions shall clearly articulate mission critical project execution requirements to include specific operational drivers or sequencing for multi-year, multi-project phased programs. Required fiscal year and justification fields are available in the IPL module to emphasize the operational year (i.e. Mission Need Date) and driver. The latest project cost and scope shall be provided on the project data sheet. Projects with follow-on phases shall be included in the Region’s Investment Plan for situational awareness and include the latest project cost and scope.

(3) Combatant Commands (CCDRs) and Navy Component Commands (NCCs) Coordination. Regions shall be familiar with CCDR Global Posture Executive Council (GPEC) requirements and develop and submit DD-1391s for CCDRs and NCCs supporting their priorities in accordance with the Navy’s MILCON Team Planning and Programming Process. This interaction will improve visibility of CCDR and NCC requirements while providing sufficient coordination through designated Executive Agents and represented Services prior to submission to OSD. NCCs will coordinate facility requirements and forward projects to the Navy Region where they are geographically aligned.

e. SMIG WG. The SMIG WG will receive briefings from the Lead Proponents/WE/Ps, CCDRs, and Regional Engineers. The SMIG WG shall use the Strategic Alignment and Guiding Principles as well as the Severity criteria and approved weightings outlined in Addendum 1 to prioritize MILCON, Special Projects and UMCs during assessments. Through a pre and post assessment governance process, the SMIG WG shall ensure all critical asset requirements are adequately accounted for and assessed. In addition, once projects are assessed, the SMIG WG will use urgency criteria and rulesets outlined in Addendum 1 to determine required investment year. Lastly, through a post-assessment process, CNIC N46 and NAVFAC will evaluate project executability. CNIC N46 will advise the SMIG WG on project executability which may influence project assessment.

4. POM-26 General Project Submission Guidance

a. For POM-26, the SMIG WG will develop and submit a five-year Requirements Plan to the SMIG Principals which separately prioritizes MILCON projects and FSRM centrally managed special projects at both enduring and contingency locations. Regions shall reference the approved POM-26 SMIG Requirements Plan included in Addendums 2 and 3 when building their POM-26 Region Requirements Plan. Projects in FY25-FY27 of the approved POM-25 SMIG Investment Plan do **not** require a formal brief to the SMIG WG unless the SMIG WG requests it. All valid unprogrammed Region requirements shall be prioritized. Programmed requirements refer to those projects in FY24 and FY25 of the most current version of the POM-24 FYDP or prior Enacted MILCONs (e.g. FY23 Enacted) for MILCON requirements and any special project identified as an FY25 requirement in the approved POM-25 SMIG Requirements Plan for FSRM requirements. The SMIG WG will validate the assessment for FY26 and FY27 projects identified in the approved POM-25 Requirements Plan. In addition, the SMIG WG will assess any mission critical emergent FY26 and FY27 requirements the Region presents during the POM-26 SMIG WG Assessment Offsite in June. The SMIG WG will integrate all requirements assessed, but not programmed, and include them as part of the POM-26 five-year Requirements Plan.

b. Decision Lens (DL) models have been combined into one model for MILCON and FSRM Special Projects for POM-26. With the implementation of a single model and the removal of Urgency, the DL weights and criteria have changed (refer to Addendum 1 for details). Please note priorities generated by Decision Lens are a tool. Region Commanders may deviate from Decision Lens with final priorities being recorded in the IPL module.

c. All capital improvement projects will continue to be submitted and assessed electronically. The EPG application and the iNFADS IPL module have been enhanced to implement the CNO's Shore Investment Guidance for capital improvement projects and incorporate feedback from POM-25. A project will only have an IPL record after a linkage with an EPG project is established. The IPL Module will be the primary means to pull data for scoring individual projects. Therefore, an EPG generated DD-1391 will be required for a project to be considered for funding during program development.

d. EPG/IPL has been synchronized with iNFADS and will be updated on a daily basis with iNFADS data (e.g. condition rating, configuration rating, capacity rating, etc.). **THE INSTALLATIONS ARE RESPONSIBLE FOR ENSURING iNFADS DATA IS ACCURATE, COMPLETE** and in accordance with standard Naval Facilities Engineering Systems Command (NAVFAC) practices and publications (located on the NAVFAC Portal).

e. Each facility identified in a project must be associated with a work type: New Footprint (NF), Sustainment (ST) (Special Projects only), Restoration & Modernization (RM), or Demolition (DE). If work is being proposed on an existing facility, then the facility must be associated with an iNFADS Navy Facility Asset (NFA) Facility ID.

f. Functionality exists in IPL to maintain project scoring and assessments for future reference. References (c) and (d) are the updated comprehensive EPG/IPL User Guides to facilitate input and validation of projects.

g. Installations shall ensure current and accurate BFRs are posted in the documents tab in EPG for each DD-1391. The Regional Engineer signature on the DD-1391 is required to validate the accuracy of the planning status level and the associated BFR/FPD and IFOM data. Regional Engineers may **NOT** delegate signatures for MILCON, LRP projects, or UMC. NAVFAC HQ AM (MILCON only; on behalf of CNIC N4/CNIC N4) will verify iNFADS BFR data currency for the respective category groups. With regard to Special Projects, Regional Engineers are required to sign all DD-1391s for projects valued at $7M or more. Signature for Special Projects below $7M may be delegated to Deputy Regional Engineers or Assistant Regional Engineers.

h. Takeaways from the POM-25 SMIG Principals brief include requirements to include in the CWE, a range and estimated cost confidence level of the project. This will be incorporated into the IPL module in POM-27. Additionally, consolidate prioritization for new platform MILCON with other non-directed/fenced MILCON. The LOE for which the project aligns to shall be included in the project description in the PDS. This will also be added to the IPL module in

for POM-27. Finally, a JRAM assessment shall be conducted with risk analysis for the impacts of the project not being programmed/funded. The CJCSM risk matrix model will be used for the JRAM assessment.

5. CNIC point of contact regarding this Guide is CDR Cody Keesee, Shore Governance Program Manager, DSN 288-4409, commercial (202) 433-4409, or e-mail cody.w.keesee.mil@us.navy.mil.

CROSBY.JASON.ALLEN.1008128401
Digitally signed by CROSBY.JASON.ALLEN.1008128401
Date: 2023.03.24 12:28:19 -04'00'

J. A. CROSBY
CAPT, CEC, USN
Director, Facilities and Environmental

Distribution:
Electronic only, via Gateway 2.0
https://g2.cnic.navy.mil/teamsites/23e5556c-bafd-41a1-905b ea7cd996608d

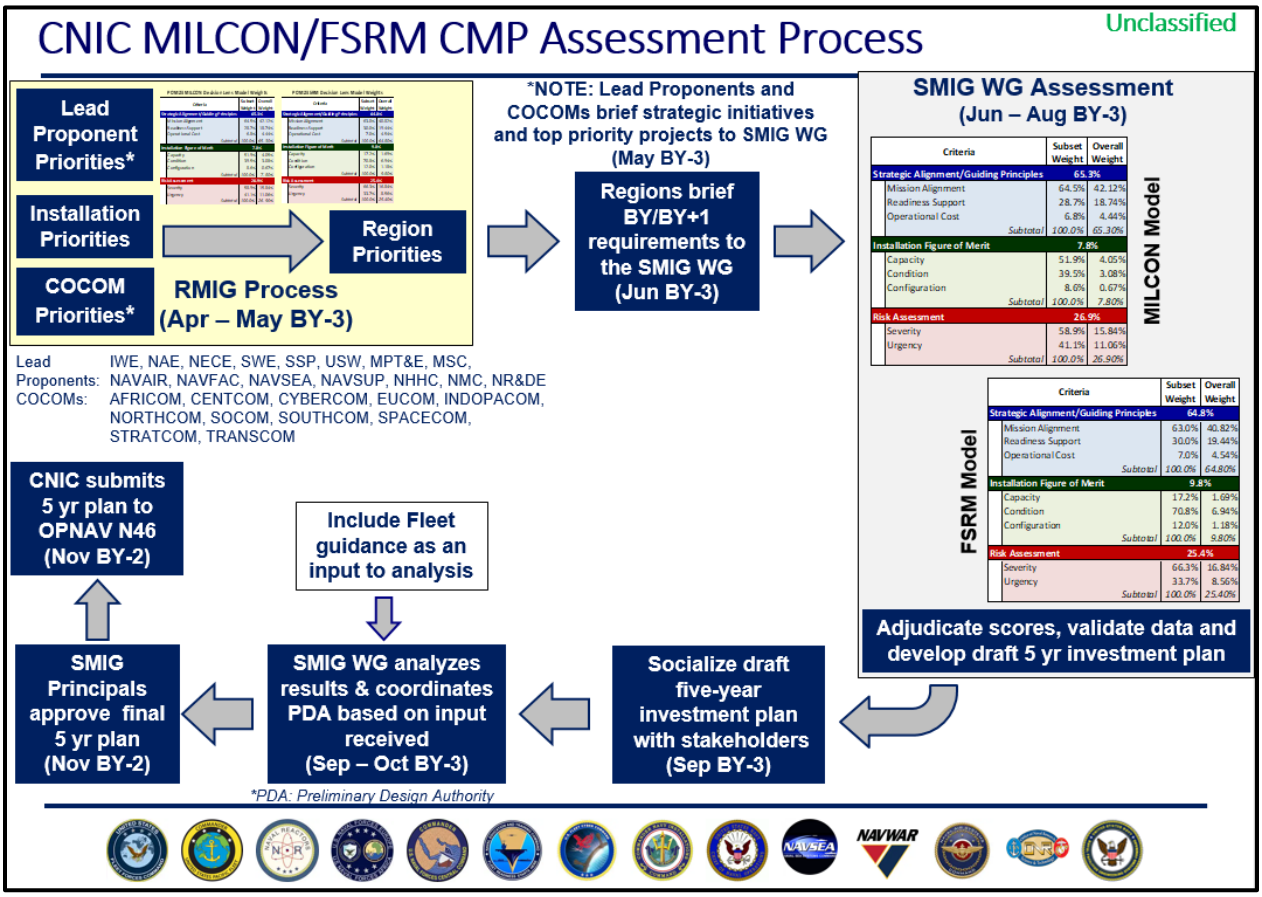

Enclosure (1)

	List of Addendums
0	POM-26 Project Development and Assessment Guide (i.e. General WARNORD)
1	POM-26 Criteria and Assessment Briefs (Definitions, Criteria Matrix, Briefing Template)
2	Military Construction (MILCON)
3	Special Projects (Sustainment, Restoration and Modernization)
4	Unspecified Minor Construction (UMC), Laboratory Revitalization Program (LRP) and Revitalize Defense Industrial Base Facilities (RDIBF)
5	Region Mission Integration Group (RMIG)
6	Installation Energy Program Summary (IEPS)
7	Naval Construction Force (NCF)
8	Facility Readiness Ratings

Enclosure (2)
